

MEASURE L

CITIZENS' BOND OVERSIGHT COMMITTEE

QUARTERLY FINANCIAL REPORT ENDING 12/31/2024

Bond Income and Expenditure Summary



SAN LUIS OBISPO COUNTY COMMUNITY COLLEGE DISTRICT

Dr. Gilbert Stork, Chair

Robert “Grigger” Jones

Clint Weirick

Dr. Dan Chernow

Ranelle Baldwin

Henry Rible

Andy Garcia-Mora

1st Issuance Bond Income and Expenditure Summary

The first series of obligation bonds was issued in March of 2015 in the amount of \$75,000,000. The bonds were sold at a premium (an amount in excess of face value) and generated an additional \$6,114,164.05. The premium can only be used for limited items and traditionally is used to cover some administrative bond costs such as the cost of issuance and the underwriter's discount. The remaining amount is required to be paid to the county treasurer for the repayment of outstanding bonds. The premiums usage is included in the summary below.

The 1st Issuance was fully spent as of June 30, 2020.

The following summary reflects projected Series A and A1 Measure L election of 2014 general obligation bond proceeds available for projects:

Sale of Series A bonds (Non-taxable)	\$72,400,000.00	
Sale of Series A-1 bonds (Federally Taxable)	2,600,000.00	
Original Issue Premium Series A	6,114,164.05	
Interest Income	909,444.20	
Miscellaneous Income	<u>650.00</u>	
Total		\$82,024,258.25

The following summary reflects major categories of expenditures:

Cost of Issuance Series A and A-1	\$ 195,185.92	
Underwriter's Discount Series A and A-1	<u>300,000.00</u>	
Total		(495,185.92)
Total Project Fund		\$81,529,072.33
Transfer for Debt Servicing		<u>(5,828,691.84)</u>
Proceeds Projected for Bond Projects		\$75,700,380.49

Construction Projects

COPs Repayment	\$11,776,478.18	
Program Management	922,101.20	
Bond Program - District	390,479.41	
NC Campus Center	31,679,062.56	
SLO Instructional Building	19,617,519.72	
Aquatic Center Complex	632,776.34	
Aquatic Center Renovation	56,370.37	
1000 Complex Renovation	65,111.10	
Site Infrastructure	328,873.37	
NC Sitework Improvements	266,622.71	
Interim Offices and Classrooms	3,354,372.31	
Interim Faculty Offices	388,389.12	
Roofing/HVAC Replacement	1,118,391.00	
9100 Building Repairs & Upgrades	256,951.00	
Bond Planning	481,552.00	
Campus Safety	168,098.70	
Hollister Adobe	28,725.00	
Technology Upgrades	1,330,279.27	
Data Center	591,876.41	
ECE Building	640,286.23	
Gym Floor Replacement	469,056.50	
Road Asphalt Improvements	703,231.90	
7300 Building Upgrades	131,170.58	
1400 Building HVAC	170,707.39	
Campus Center SLO	20,950.00	
Trades & Technology (NCC)	66,956.12	
NC Instructional Building	43,992.00	
Total Construction		<u>(75,700,380.49)</u>
Total Remaining		<u>\$0.00</u>

2nd Issuance Bond Income and Expenditure Summary

The second series of obligation bonds was issued in February of 2018 in the amount of \$73,000,000. The bonds were sold at a premium (an amount in excess of face value) and generated an additional \$7,451,575.30. The premium can only be used for limited items and traditionally is used to cover some administrative bond costs such as the cost of issuance and the underwriter's discount.

The 2nd Issuance was fully spent as of March 31, 2023.

The following summary reflects projected Series B Measure L election of 2014 general obligation bond proceeds available for projects:

Sale of Series B bonds	\$73,000,000.00	
Original Issue Premium Series B	7,451,575.30	
Interest Income	2,634,033.00	
Cost of Issuance Returned	<u>4,404.49</u>	
Total		\$83,090,012.79

The following summary reflects major categories of expenditures:

Cost of Issuance Series B	\$ 196,909.00	
Underwriter's Discount Series B	<u>288,350.00</u>	
Total		<u>(485,259.00)</u>
Total Project Fund		\$82,604,753.79
Transfer for GO Debt Servicing		<u>(7,163,225.30)</u>
Proceeds Projected for Bond Projects		\$75,441,528.49

Construction Projects

COPs Repayment	\$6,035,788.01	
Program Management	3,015,355.17	
Bond Program - District	693,087.41	
Technology Upgrades	5,600,000.00	
Fiber Loop Programming	3,547.25	
Aquatic Center Complex	10,027,821.28	
1000 Complex Renovation	1,880,517.31	
2000 Complex Renovation	5,068,635.68	
ADA Upgrades	2,906,058.79	
Switchgear Replacement	1,447,491.62	
Switchgear 8 Emergency	153,024.54	
Data Center	7,283,951.50	
ECE Building	15,391,082.33	
NC Sitework Improvements	3,550,182.50	
NC Chiller Line Repairs	19,436.72	
Wayfinding	387,120.41	
Site Infrastructure	658,681.99	
Interim Offices and Classrooms	133,774.01	
Interim Faculty Offices	33,733.32	
Gym Floor Replacement	109,399.48	
Campus Center SLO	1,843,385.85	
Bond Planning	181,700.00	
Road Asphalt Improvements	2,868,310.92	
Asphalt Refurbishing	87,423.00	
Electric Vehicle Charging Station	115,777.79	
Hollister Adobe	233,317.33	
7100 Building Electrical	120,637.50	
9100 Building Repairs & Upgrades	458,799.21	
1400 Building Circuit Breaker	14,062.28	
SLO Campus Interiors	321,476.40	
Roofing & HVAC Upgrades	4,288,445.04	
Campus Safety	20,784.31	
7500 Building Renovation	488,719.54	
Total Construction		<u>(\$75,441,528.49)</u>
Total Remaining		<u>\$0.00</u>

3rd Issuance Bond Income and Expenditure Summary

The third series of obligation bonds was issued in February of 2021 in the amount of \$70,000,000. The bonds were sold at a premium (an amount in excess of face value) and generated an additional \$6,263,524.15. The premium can only be used for limited items and traditionally is used to cover some administrative bond costs such as the cost of issuance and the underwriter’s discount. The remaining amount is required to be paid to the county treasurer for the repayment of outstanding bonds. The premiums usage is included in the summary below. Interest income in the amount of \$263,667.20 has been received for the 2nd Quarter of Fiscal Year 2024-25. The following summary reflects projected Series C Measure L election of 2014 general obligation bond proceeds available for projects:

Sale of Series C bonds	\$70,000,000.00	
Original Issue Premium Series C	6,263,524.15	
Interest Income	3,679,303.92	
Cost of Issuance Returned	<u>6,104.03</u>	
Total		\$79,948,932.10

The following summary reflects major categories of expenditures:

Cost of Issuance Series C	\$ 195,000.00	
Underwriter’s Discount Series C	<u>276,500.00</u>	
Total		<u>(471,500.00)</u>
Total Project Fund		\$79,477,432.10
Transfer for GO Debt Servicing		<u>(5,987,024.15)</u>
Proceeds Projected for Bond Projects		\$73,490,407.95


Construction Projects

Program Management	4,207,570.76	
Bond Program - District	550,309.25	
Bond Planning	182,032.00	
Technology Upgrades	1,802,354.72	
Interim Offices	86,376.00	
Interim Faculty Offices	26,400.00	
Campus Center SLO	29,576,474.17	
Wayfinding & Signage	885,877.04	
Roofing & HVAC District Wide	4,787,892.79	
3100-3400 Bldg. Renovation	227,871.50	
NC Instructional Building	1,314,661.16	
Switchgear Replacement	727,931.71	
ADA Upgrades	537,870.04	
Cafeteria Equipment Design	14,100.00	
Interior Upgrades	853,610.22	

Total Construction		<u>(45,781,331.36)</u>
Total Remaining		<u>\$27,709,076.59</u>

San Luis Obispo County Community College District
 Measure L Bond (2018) Phase 3 Estimated Budget
 as of December 31, 2024

Project	Estimated Budget	Current Qtr Expenditures	Total Expenditures	Remaining Comt/Encum	Remaining Balance
Program Management	\$ 5,931,256	\$ 40,964	\$ 4,207,571	\$ 830,303	\$ 893,382
Bond Program District	550,309	-	550,309	-	-
Bond Planning	218,115	-	182,032	36,083	-
Interim Offices	86,376	-	86,376	-	-
Interim Faculty Offices	26,400	-	26,400	-	-
Technology Upgrades	2,400,000	155,352	1,802,355	572,092	25,553
Campus Center SLO	47,067,297	5,223,073	29,576,474	14,895,989	2,594,834
Roofing & HVAC District Wide	7,822,625	152,372	4,787,893	969,299	2,065,433
Wayfinding & Signage	898,120	37,654	885,877	12,243	-
3100-3400 Bldg. Renovation	1,513,493	8,829	227,872	1,285,621	-
NC Instructional Building	1,314,831	35,140	1,314,661	170	-
Switchgear Replacement	1,770,254	5,892	727,932	926,650	115,672
ADA Upgrades	621,037	-	537,870	83,167	-
Interior Upgrades	1,562,034	43,469	853,610	181,837	526,587
Cafeteria Equipment Design	14,100	-	14,100	-	-
Total	\$ 71,796,247	\$ 5,702,745	\$ 45,781,331	\$ 19,793,454	\$ 6,221,461

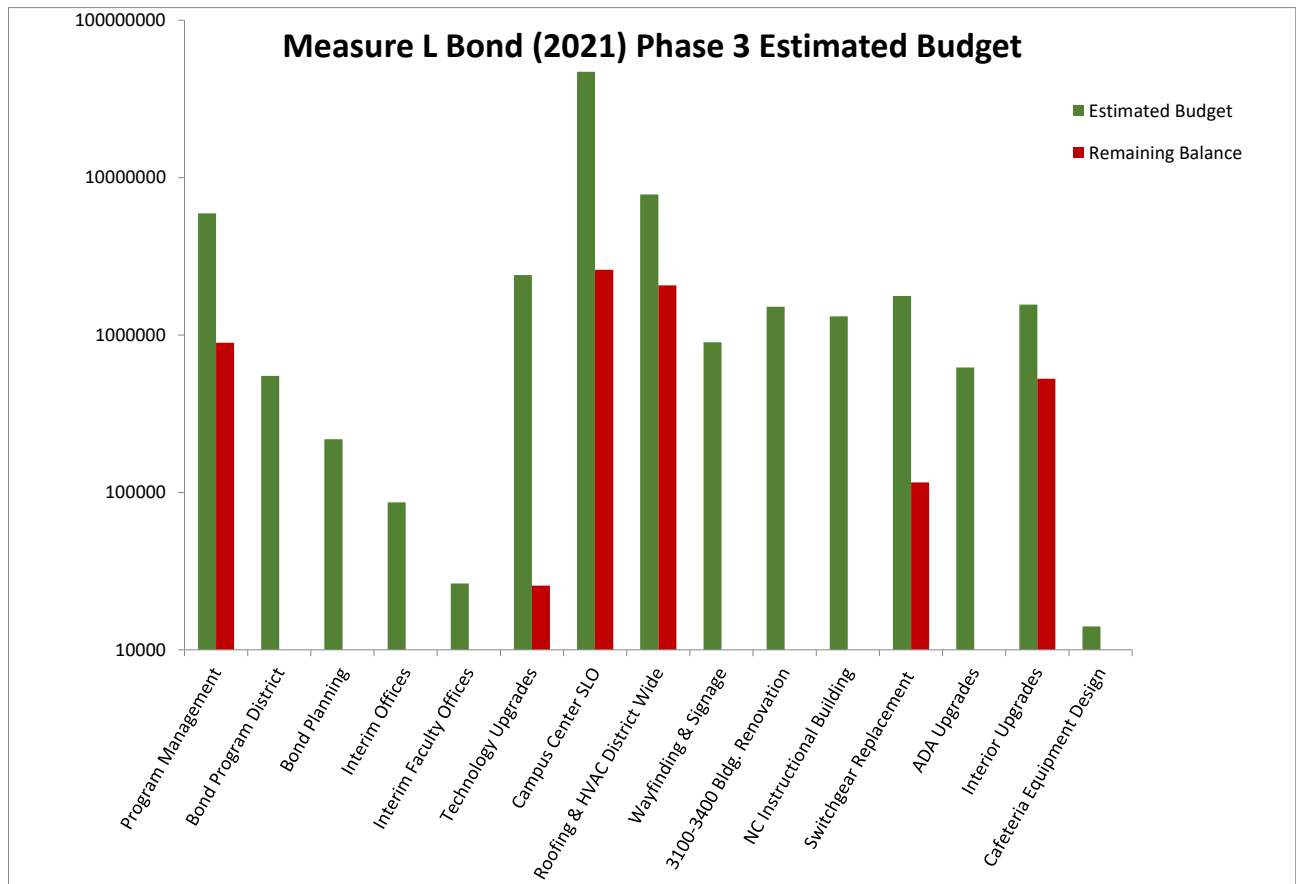

4th Issuance Bond Income and Expenditure Summary

The fourth series of obligation bonds was issued in February of 2024 in the amount of \$57,000,000. The bonds were sold at a premium (an amount in excess of face value) and generated an additional \$6,552,005.40. The premium can only be used for limited items and traditionally is used to cover some administrative bond costs such as the cost of issuance and the underwriter's discount. The remaining amount is required to be paid to the county treasurer for the repayment of outstanding bonds. The premiums usage is included in the summary below. Interest income in the amount of \$511,824.57 has been received for the 2nd Quarter of Fiscal Year 2024-25. The following summary reflects projected Series D Measure L election of 2014 general obligation bond proceeds available for projects:

Sale of Series D bonds	\$57,000,000.00	
Original Issue Premium Series D	6,552,005.40	
Interest Income	<u>1,789,169.87</u>	
Total		\$65,341,175.27

The following summary reflects major categories of expenditures:


Cost of Issuance Series D	\$ 195,000.00	
Underwriter's Discount Series D	<u>213,750.00</u>	
Total		<u>(408,750.00)</u>
Total Project Fund		\$64,932,425.27
Transfer for GO Debt Servicing		<u>(6,552,005.40)</u>
Proceeds Projected for Bond Projects		\$58,380,419.87

Construction Projects

Program Management	234,403.50	
Bond Program – District	229,081.45	
Bond Planning	14,059.50	
Interim Office Housing	43,188.00	
Faculty Interim Housing	8,800.00	
Technology Upgrades	493,617.30	
NC Instructional Bldg.	848,908.20	
3100-3400 Bldg. Renovation	684,499.00	
Interior Upgrades Modernization	229,324.25	
Roofing & HVAC	223,207.28	
Site Infrastructure	95,697.00	
Total Construction		<u>(3,104,785.48)</u>
Total Remaining		<u><u>\$55,275,634.39</u></u>

San Luis Obispo County Community College District
 Measure L Bond (2024) Phase 4 Estimated Budget
 as of December 31, 2024

Project	Estimated Budget	Current Qtr Expenditures	Total Expenditures	Remaining Comt/Encum	Remaining Balance
Program Management	\$ 1,885,702	\$ (187,597)	\$ 234,404	\$ 1,351,299	\$ 300,000
Bond Program District	950,000	63,648	229,081	720,919	-
Bond Planning	53,300	4,172	14,060	39,240	-
Interim Offices	164,158	-	43,188	120,970	-
Interim Faculty Offices	38,378	8,800	8,800	29,578	-
Technology Upgrades	1,360,000	214,304	493,617	596,883	269,500
NC Instructional Building	20,914,298	365,696	848,908	18,923,440	1,141,950
3100-3400 Bldg. Renovation	26,990,904	242,932	684,499	3,238,736	23,067,669
Interior Upgrades Modernization	2,616,563	89,898	229,324	688,019	1,699,220
Roofing & HVAC District Wide	1,056,246	20,147	223,207	721,539	111,500
Site Infrastructure	1,340,986	33,703	95,697	383,364	861,925
Total	\$ 57,370,535	\$ 855,704	\$ 3,104,785	\$ 26,813,985	\$ 27,451,764

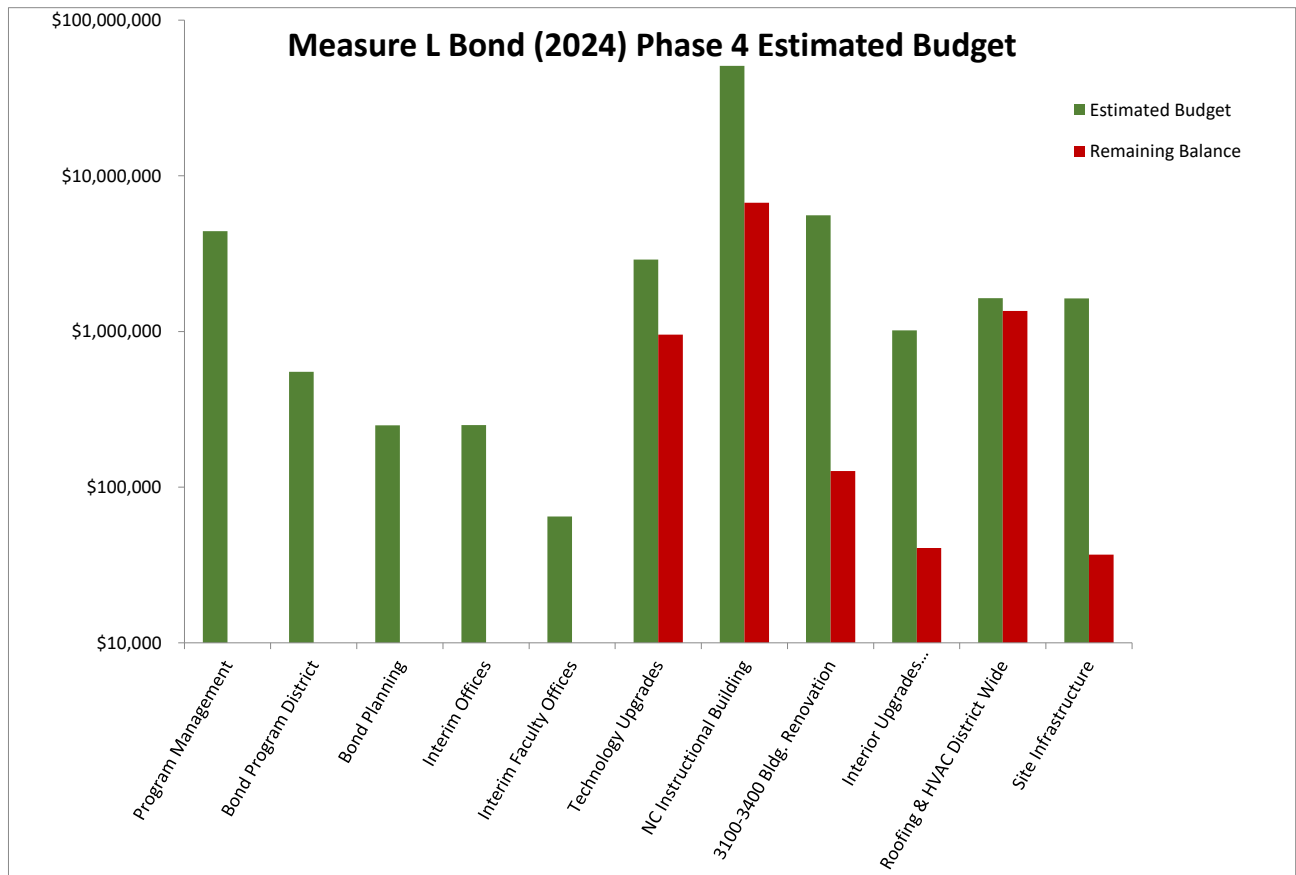

San Luis Obispo County Community College District
Measure L Bond Total Project Cost
as of December 31, 2024

Project Name	Total Budget	1st Issuance Bond Expenses	2nd Issuance Bond Expenses	3rd Issuance Bond Expenses	4th Issuance Bond Expenses	Total Project Bond Expenses
NC Campus Center	\$ 31,679,063	\$ 31,679,063				\$ 31,679,063
SLO Instructional Building	19,617,520	19,617,520				19,617,520
Aquatic Center Complex	10,660,598	632,776	10,027,821			10,660,598
1000 Complex Renovation	1,945,628	65,111	1,880,517			1,945,628
2000 Complex Renovation	5,068,636		5,068,636			5,068,636
Data Center	7,875,828	591,876	7,283,952			7,875,828
ECE Building	16,031,369	640,286	15,391,082			16,031,369
NC Chiller Line Repair	19,437		19,437			19,437
COPs Loan Repayment	17,812,266	11,776,478	6,035,788			17,812,266
Interim Offices and Classrooms	3,738,680	3,354,372	133,774	86,376	43,188	3,617,710
Interim Faculty Offices	486,900	388,389	33,733	26,400	8,800	457,322
Bond Program - District	2,583,876	390,479	693,087	550,309	229,081	1,862,958
Program Management	11,754,414	922,101	3,015,355	4,207,571	234,404	8,379,431
Technology Upgrades	10,690,279	1,330,279	5,600,000	1,802,355	493,617	9,226,251
Site Infrastructure	2,328,541	328,873	658,682		95,697	1,083,252
NC Sitework Improvements	3,816,805	266,623	3,550,183			3,816,805
Emergency Repairs						-
SLO Campus Center	48,931,633	20,950	1,843,386	29,576,474		31,440,810
ADA Upgrades	3,527,096		2,906,059	537,870		3,443,929
3100-3400 Building Renovation	28,504,397			227,872	684,499	912,371
Campus Interiors Upgrades	4,500,073		321,476	853,610	229,324	1,404,411
Fiber Loop Programming	3,547		3,547			3,547
Wayfinding & Signage	1,285,240		387,120	885,877		1,272,997
Hollister Adobe	262,042	28,725	233,317			262,042
Gym Floor Replacement	578,456	469,057	109,399			578,456
Bond Planning	934,667	481,552	181,700	182,032	14,060	859,344
Switchgear Replacement	3,217,746		1,447,492	727,932		2,175,423
Switchgear & Emergency	153,025		153,025			153,025
Aquatic Center - Renovation	56,370	56,370				56,370
Roofing/HVAC Replacement 1st Issuance	1,118,391	1,118,391				1,118,391
9100 Building Repairs & Upgrades	715,750	256,951	458,799			715,750
NC Instructional Building (T&T)	22,340,077	110,948		1,314,661	848,908	2,274,517
Campus Safety	188,883	168,099	20,784			188,883
Road Asphalt Improvements	3,571,543	703,232	2,868,311			3,571,543
Asphalt Refurbishing	87,423		87,423			87,423
7100 Building Electrical	120,638		120,638			120,638
7300 Building Upgrades	131,171	131,171				131,171
7500 Building Renovation	488,720		488,720			488,720
Roofing & HVAC Repairs District Wide	13,167,316		4,288,445	4,787,893	223,207	9,299,545
Electric Vehicle Charging Station	115,778		115,778			115,778
1400 Building HVAC	184,770	170,707	14,062			184,770
Cafeteria Equipment Design	14,100			14,100		14,100
TOTALS	\$ 280,308,691	\$ 75,700,380	\$ 75,441,528	\$ 45,781,331	\$ 3,104,785	\$ 200,028,026
